Job #317616 | Penn Valley Pump | 8/25/14
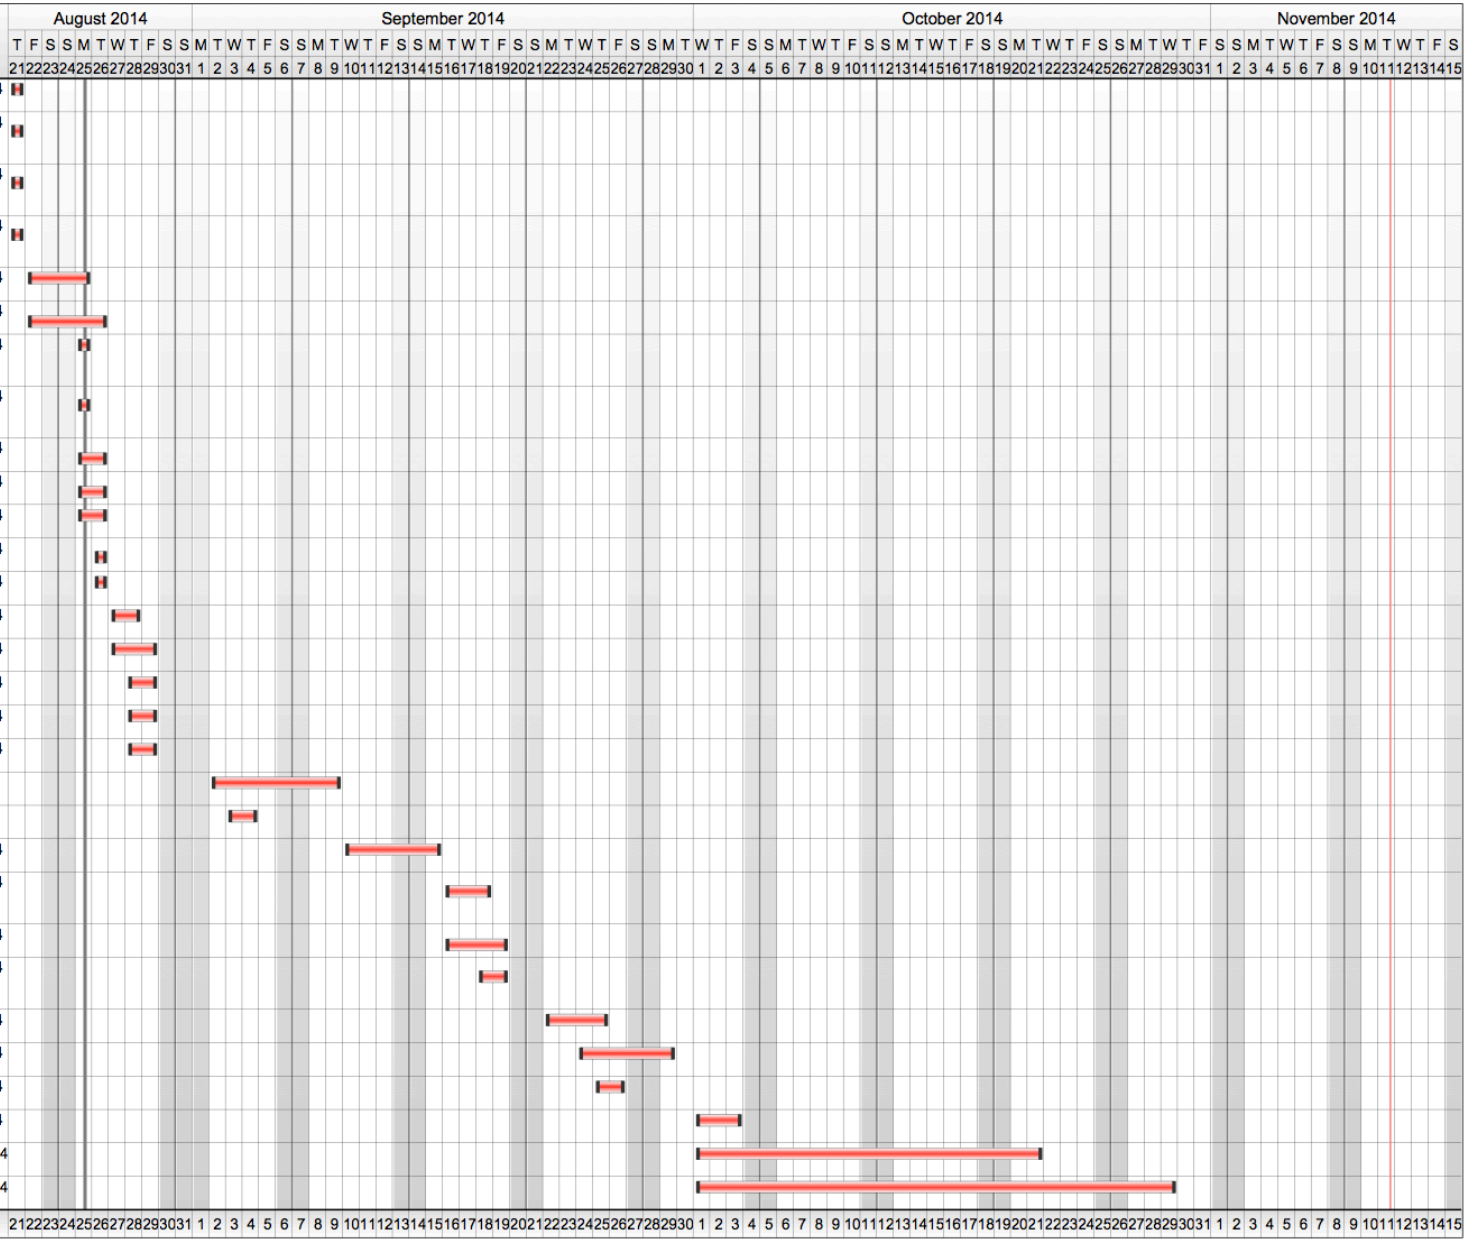
Activity Name	Duration (Days)	Start Date	Finish Date
Pick Up Building Permit	1.00	8/21/14	8/21/14
Pick Up Signed Engineered Drawings	1.00	8/21/14	8/21/14
Pre-Construction Meeitng with Carroll Engineering	1.00	8/21/14	8/21/14
Pre-Construction Meeting with Building Inspector	1.00	8/21/14	8/21/14
Lay Out	2.00	8/22/14	8/25/14
Tree Removal	3.00	8/22/14	8/26/14
Set Up Temporary Contractor's Toilet	1.00	8/25/14	8/25/14
Owner to Have His Temporary Toilets in Place	1.00	8/25/14	8/25/14
Silt Fencing Installed	2.00	8/25/14	8/26/14
Construction Trailer Set on Site	2.00	8/25/14	8/26/14
Construction Entrance	2.00	8/25/14	8/26/14
Clearing & Grubbing	1.00	8/26/14	8/26/14
Pump Out Septic Tank	1.00	8/26/14	8/26/14
Remove Septic Tank	2.00	8/27/14	8/28/14
Demolition of Exterior Structures	3.00	8/27/14	8/29/14
Get Building to Sub Pad	2.00	8/28/14	8/29/14
Pole RElocation	2.00	8/28/14	8/29/14
Temporary Trailer Power	2.00	8/28/14	8/29/14
Start Footings	6.00	9/2/14	9/9/14
Install Sleeves for Footings	2.00	9/3/14	9/4/14
Foundation Block	4.00	9/10/14	9/15/14
Saw Cut Existing Window Openings	3.00	9/16/14	9/18/14
Underground Plumbing Drains	4.00	9/16/14	9/19/14
Remove Bottom Blocks at New Openings	2.00	9/18/14	9/19/14
Pre-pour Interior Slab 6"	4.00	9/22/14	9/25/14
Pre-pour 4" Thick Slab	4.00	9/24/14	9/29/14
Loose Lintel Delivery	2.00	9/25/14	9/26/14
Set Exterior Steel Door Jambs	3.00	10/1/14	10/3/14
Building Block	15.00	10/1/14	10/21/14
Metal Stud Framing	21.00	10/1/14	10/29/14
